

One portal for how GSQ plants run DD&T

Leadership still prepares business reviews by stitching Jira, SPOT, site Power Apps, Power BI, and PowerPoint. The cost is not software — it is leadership time and inconsistent answers in the same meeting.

Why	What	Who	Where
Purpose Run the review from a maintained system of record, not a slide factory.	The Glass One site-aware portal. Ten views. Reuse what exists; add what is missing.	Sponsors Joel Vincent • Executive sponsor Dean Santoro • Product lead	SPOT 1063647 Already live • Plan phase. Do not open a second project.

This is A single pane of glass for 18 GSQ Manufacturing & Labs sites. Site becomes a drop-down. Budget and Gantt sit on the same row. Site Heads type commentary and asks in the same portal. Thousand Oaks is the first business-review system of record.	This is not A new strategy, a second Jira, or a second SPOT. The portal does not overwrite dates or money. The \$42k / 6-week figure is a thin shell only — it cannot prove Jira + SPOT + EDB together.
--	---

The value is hours back — proven first at Thousand Oaks

9,000	42	\$168k	30,000
hours / year Filed value case • 18 sites ~500 hours per site per year	hours / site / month Deck assembly and status chasing the portal is meant to remove	Band B envelope 10–12 weeks • ~2.5 FTE Recommended Marketplace order	hours total FY26 3,000 • FY27–29 9,000/yr On the SPOT 1063647 record


Investment options — fund the product that can stop the decks

Option	What you get	Time	Indicative cost
A. Thin shell	Site drop-down + wrap today's tabs. No SPOT, no EDB, no Site Head input.	6 weeks • 1 FTE	~\$42k
B. Recommended MVP	Live Jira + SPOT, combined Gantt, Capability, Site input, TO review freeze.	10–12 weeks • ~2.5 FTE	~\$155–168k
C. Full case	Band B + EDB data-product bind + production network roadmap.	12 weeks • ~3 FTE	~\$196k

Business case §1 already quotes ~\$168k / 6–12 weeks. Section 9 quotes ~\$40k / 6 weeks. Those are different products. Recommend Band B at the \$168k envelope. Do not approve Band A if the test is “executives stop building decks.” EDB binds as a gated increment inside the same order; the Capability Tracker embed is the fallback so the meeting still has an adoption view.

Value hypothesis on SPOT 1063647 • COP = Productivity Improvements • Capture start 1 Dec 2026

One Glass. Three systems of record. One write path.

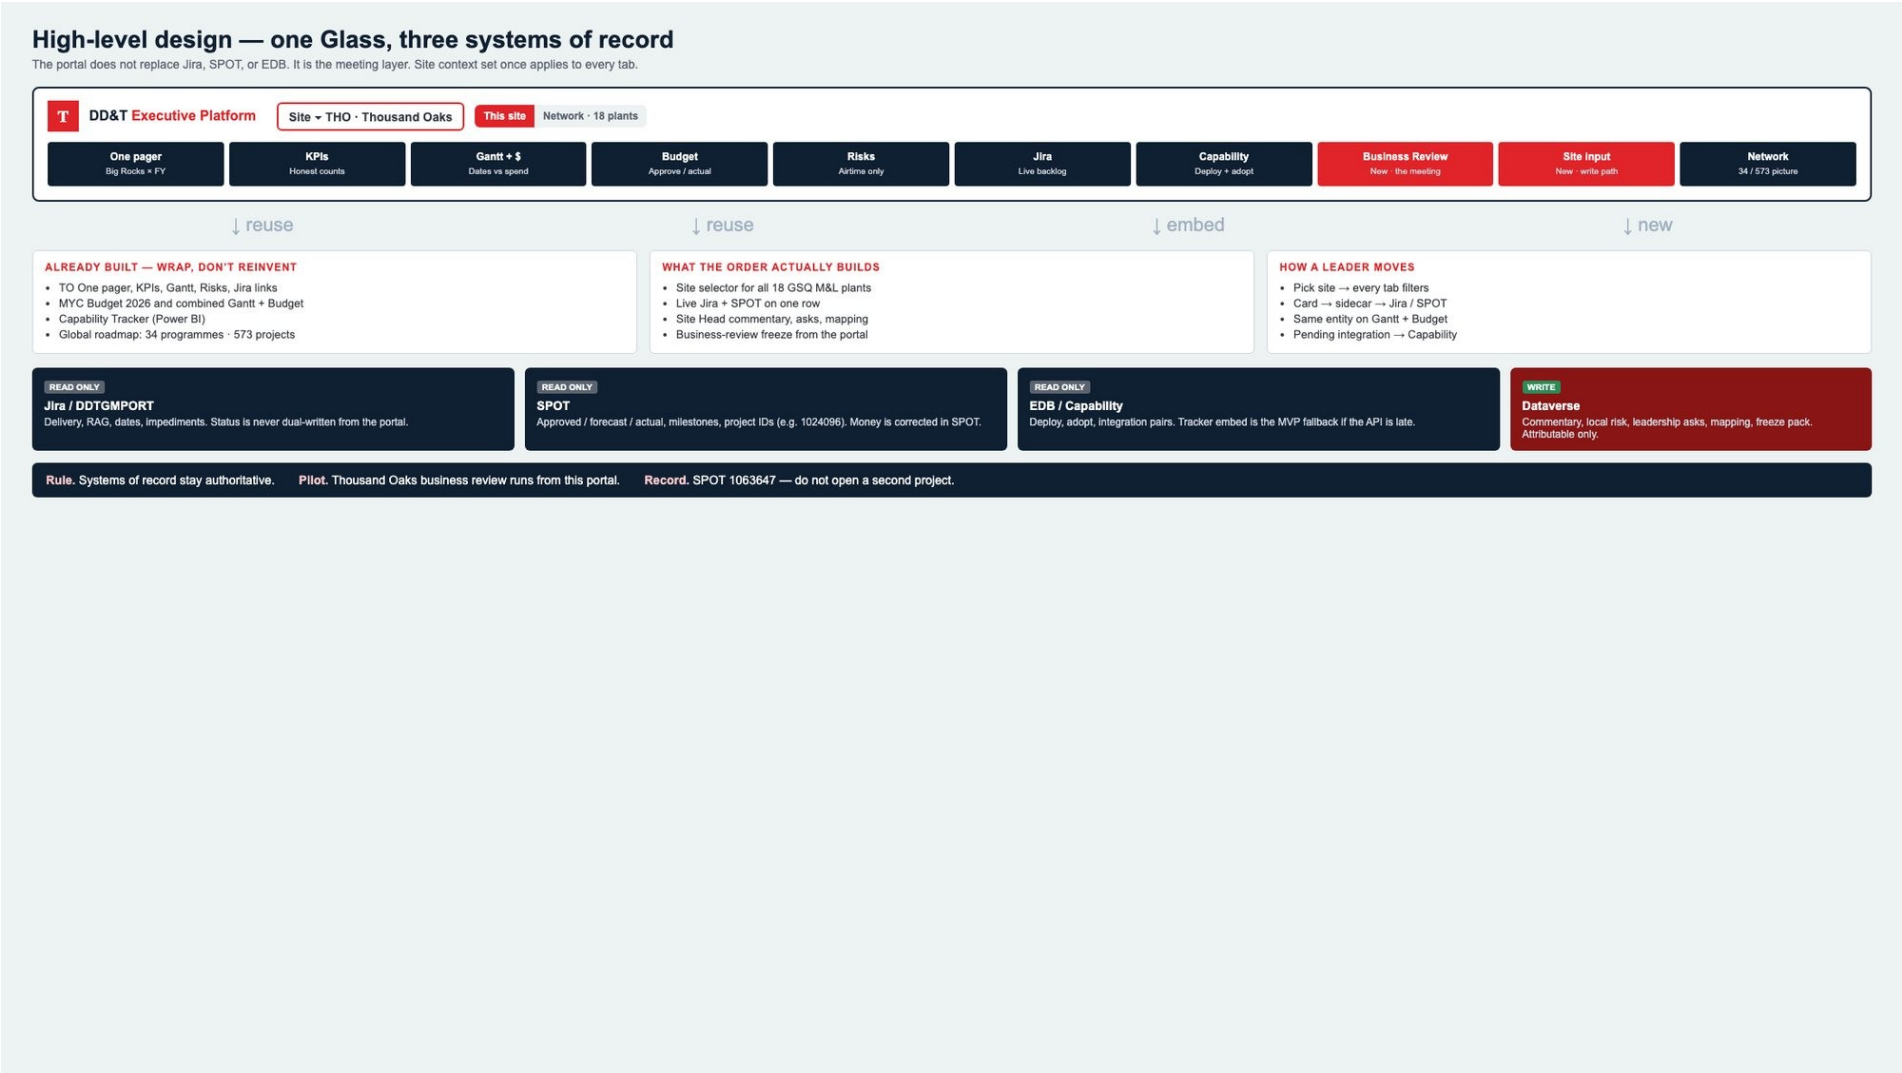

Read-only: Jira · SPOT · EDB/Capability Write: Dataverse commentary, asks, mapping, freeze pack

Same chrome on every tab. Site set once. The meeting runs here.

TARGET MOCKUP • NOT A LIVE APP • WHAT THE DEVELOPER BUILDS

SITE SELECTOR • BUDGET / CAPABILITY / BUSINESS REVIEW / SITE INPUT ADDED TO THE CURRENT ONE PAGER SHELL

T

DD&T Executive Platform

Jira 2 minSPOT 41 minEDB 1hSite Head 14:02Dean Santoro • Site DD&T

SITE — 18 GSQ M&L
THO • Thousand Oaks

This siteNetwork

DD&T Roadmap FY26–FY28+
Executive roadmap • Big Rocks × fiscal year • layout writes mapping only

Open Jira board

One pagerStatus KPIsGantt + BudgetBudgetRisksJiraCapabilityBusiness ReviewNEWSite inputNEWNetwork

Search project / SPOTAll fiscal yearsAll platformsAll statusAll Big Rocks

6 BIG ROCKS

FY2026
BUILD
FOUNDATION

FY2027
SCALE &
INTEGRATE

FY2028+
TRANSFORM

ONE DAY
BATCH RELEASE

LAB OF THE
FUTURE

PREDICTIVE
MAINTENANCE

RAPID DIGITAL
TECH TRANSFER

INVENTORY
OPTIMIZATION

POWER OF
DIGITAL TWINS

MES Elaprse DS
SPOT 1024096 • DDTTO-12

NYMI Batch
SPOT 1042101

Labware LIMS
DDTTO-31

LabX scales
Planning

TO APMS
SPOT 1041357

LPMS rollout
Leadership

TO SAIL — FDP
DDTTO-08

Takami
DDTTO-58 • unmapped FY?

SAP warehouse
Site-led

Discoverant feed
Planning

MES ↔ SAIL
Integration

Smart QC
North Star

No projects in this Big Rock / year

Phoenix
SPOT - \$436k

Takami inventory
Programme

SIMCA Online
Digital twin

No projects in this Big Rock / year

Paperless Ops
Planning

RTMS expand
North Star

No projects in this Big Rock / year

No projects in this Big Rock / year

Enterprise data twin
EDB

Selected • MES Elaprse DS

OwnerSite MES lead

StatusOn track

JiraDDTTO-12

SPOT1024096

Big RockOne Day Batch Release

FY swimlaneFY26 • mapping

Go-liveJira date • Q3 FY26

Replace paper batch steps on Elaprse DS. Value sits in Jira; spend sits in SPOT.

Drag moves Big Rock × FY mapping only. Jira dates and SPOT money do not change.

Open in Gantt + Budget

Capability • MES

Open Jira issue

On trackMonitor closelyLeadership attentionBlockedPlanning / no statusComplete

Key challenges: Communication • Change management • Leadership engagement

One pager
Big Rocks × FY
KPIs
Honest counts

Gantt + Budget
Dates vs spend
Risks
Airtime only

Budget
Approve / actual
Jira
Live backlog

Capability
Deploy + adopt
Site input
Only write path — new

Business Review
The meeting — new
Network
34 programmes / 573 projects

Target mockup — not a live app. Full view specs and live source screenshots are in the Design Blueprint.

Approve Band B. Pilot at Thousand Oaks. Keep SPOT 1063647.

01 Fund Band B	02 Pilot Thousand Oaks	03 Keep 1063647	04 Authorize onboarding
\$155–168k • 10–12 weeks to the design blueprint.	First business-review system of record. UAT weeks 9–10.	File the funding request here. Align CAPEX to one number.	AIDPG Initiative → 1063647. Pattern-Fit • Intake gate.

Go / no-go for Release 2

One TO business review runs from the portal.	Site Head commentary is attributable.	Jira, SPOT, and Capability match in the room.	Leadership agrees the pattern scales.
--	---------------------------------------	---	---------------------------------------

Next artefact is the AIDPG Initiative pointing at 1063647 — not a second SPOT. Week-1 work is a field workshop with PMO on Jira fields, SPOT access, and mapping quality. API access is the critical path; if it slips, the calendar slips.
